HAMBY-LYNCH PUBLIC SAFETY COMPLEX

PROGRESS UPDATE
DESIGN DEVELOPMENT

CATOOSA
PRIDE. PROGRESS. PROMISE.

© 2022 GH2 Architects, LLC

GH2 ARCHITECTS

PROJECT PROGRESS TO DATE

- **APRIL BOND APPROVAL**
- **MAY CONTRACT APPROVAL**
- **JUNE –JULY COMPLETED SCHEMATIC DESIGN 30%**
  - SITE PLAN UPDATES
  - FLOOR PLAN REVISIONS
  - UTILITY EXPANSION
  - RENDERING UPDATE
  - CIVIL DESIGN AND COORDINATION
  - MULTIPLE OWNER, ARCHITECT, AND CM DESIGN MEETINGS
    - CM PROVIDED COST ESTIMATE UPDATE
- **AUGUST – SEPT. COMPLETED DESIGN DEVELOPMENT 25% (55% TOTAL COMPLETION)**
  - MEP AND STRUCTURAL SYSTEMS COORDINATION
  - INTERIOR RENDERINGS AND MATERIAL SELECTION
  - OWNER REQUESTED SITE PLAN REVISION
  - TECHNOLOGY DESIGN AND COORDINATION
  - EQUIPMENT SELECTION AND REVIEW
  - CONTINUED REFINEMENT AND DEVELOPMENT OF PROJECT DESIGN
  - MULTIPLE OWNER, ARCHITECT, AND CM DESIGN MEETINGS
    - CM PROVIDED COST ESTIMATE UPDATE

OVERALL REVIEW

GH2 ARCHITECTS

PLANNED PROJECT PROGRESS

- **CONSTRUCTION DOCUMENTS**
  - DESIGN TEAM PRODUCING CONSTRUCTION DOCUMENTS
  - 60% CONSTRUCTION DOCUMENTS TO CM OCTOBER 17TH
    - CM TO UPDATE COST ESTIMATE
  - ISSUE EARLY GRADING PACKAGE
  - ISSUE DESIGN PACKAGES INCLUDING DRAWING VOLUMES AND PROJECT MANUAL TO CM FOR BIDDING AND PERMITTING
- **BIDDING AND PERMITTING**
  - RECEIVE BIDS REVIEW WITH CITY DESIGN TEAM AND CITY COUNCIL
  - APPLY FOR PERMIT TO ALL JURSIDICTIONS
- **CONSTRUCTION**
  - EARLY GRADING PACKAGE CONSTRUCTION STARTS
  - CONSTRUCTION ON BUILDING PACKAGE STARTS

OVERALL SITE RENDERING

© 2022 GH2 Architects, LLC

GH2 ARCHITECTS

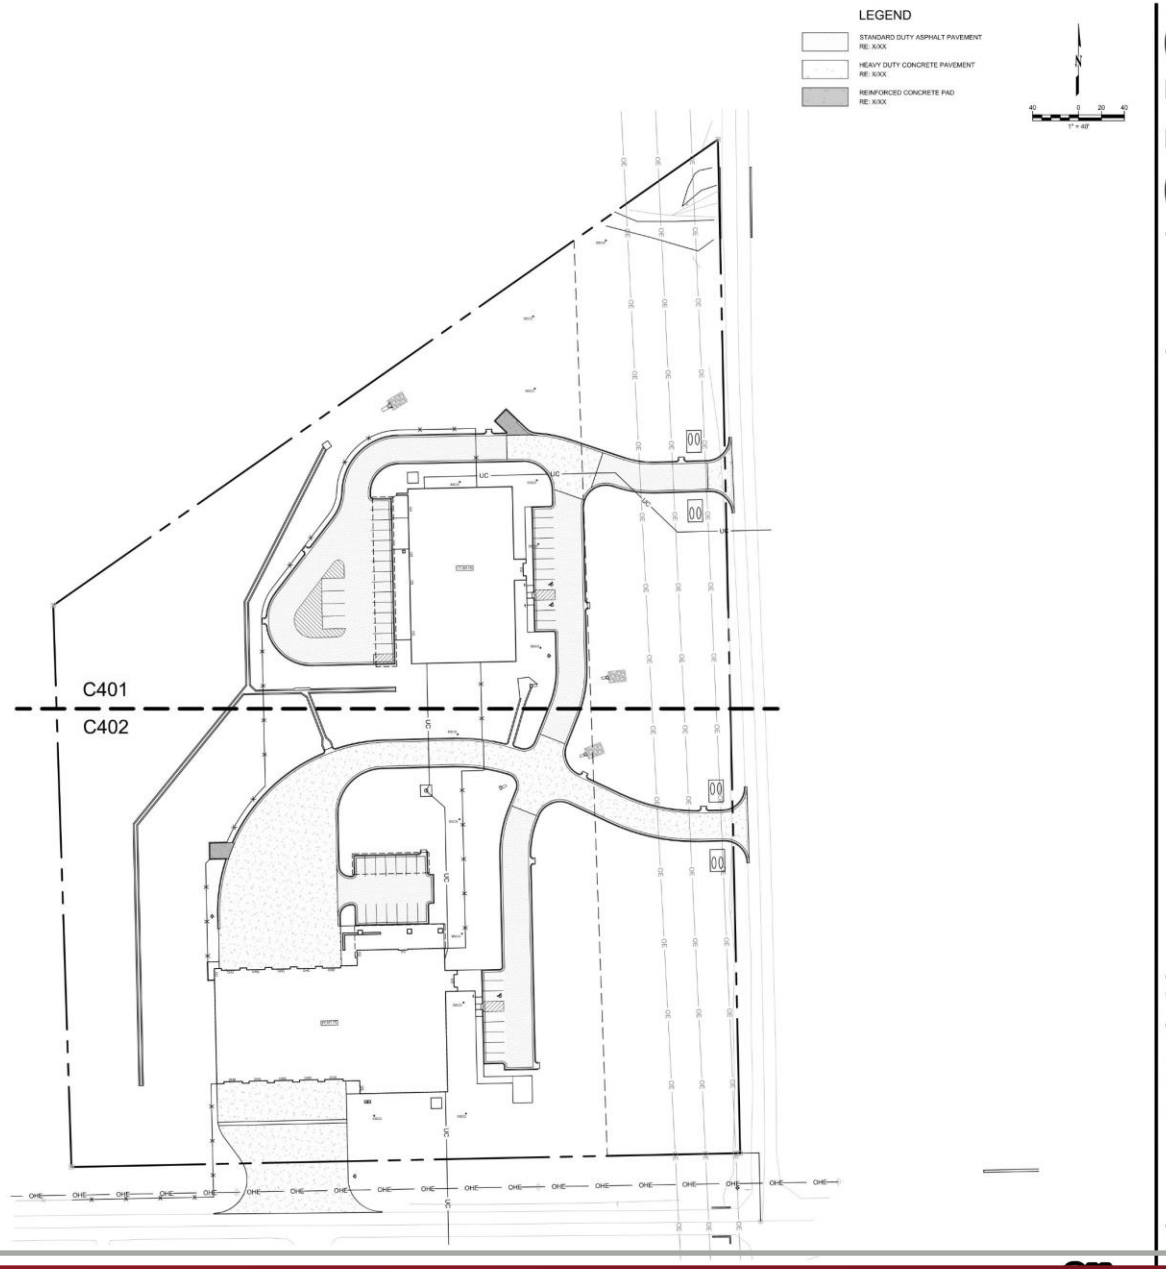

GH2 ARCHITECTS

INTERIM REVIEW ONLY

THESE DOCUMENTS ARE INCOMPLETE. THEY ARE NOT INTENDED TO BE USED FOR PERMIT, BIDDING, OR CONSTRUCTION.

HAMBY LYNCH PUBLIC SAFETY COMPLEX, VOL I.

N. 193rd E Ave. and E Pine St.
Catoosa, OK 74015

GH2 ARCHITECTS
GH2.COM

GH2 PROJECT NUMBER:
20210238

ISSUE DATE:
09/13/2022

ISSUE:
DESIGN DEVELOPMENT

OTHER ISSUE DATES:

NO.	DESCRIPTION	DATE

SHEET NAME:
Overall Site Plan

SITE PLAN

GH2 ARCHITECTS

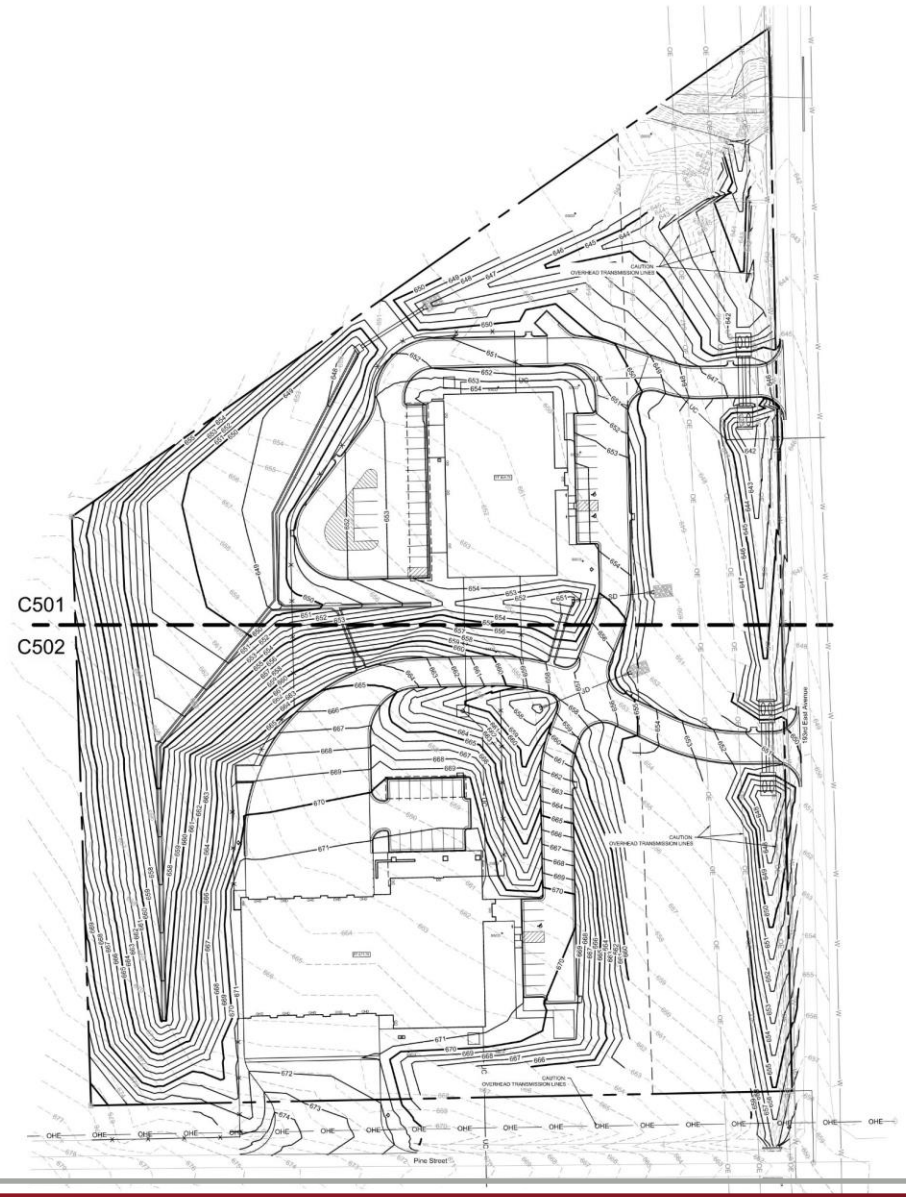

GH2 ARCHITECTS

INTERIM REVIEW ONLY

THESE DOCUMENTS ARE INCOMPLETE. THEY ARE NOT INTENDED TO BE USED FOR PERMIT, BIDDING, OR CONSTRUCTION.

HAMBY LYNCH PUBLIC SAFETY COMPLEX, VOL I.

N. 193rd E Ave. and E Pine St.
Catoosa, OK 74015

GH2 ARCHITECTS
GH2.COM

GH2 PROJECT NUMBER:
20210238

ISSUE DATE:
09/13/2022

ISSUE:
DESIGN DEVELOPMENT

OTHER ISSUE DATES:

NO.	DESCRIPTION	DATE

Call before you dig.

GRADING PLAN

GH2 ARCHITECTS

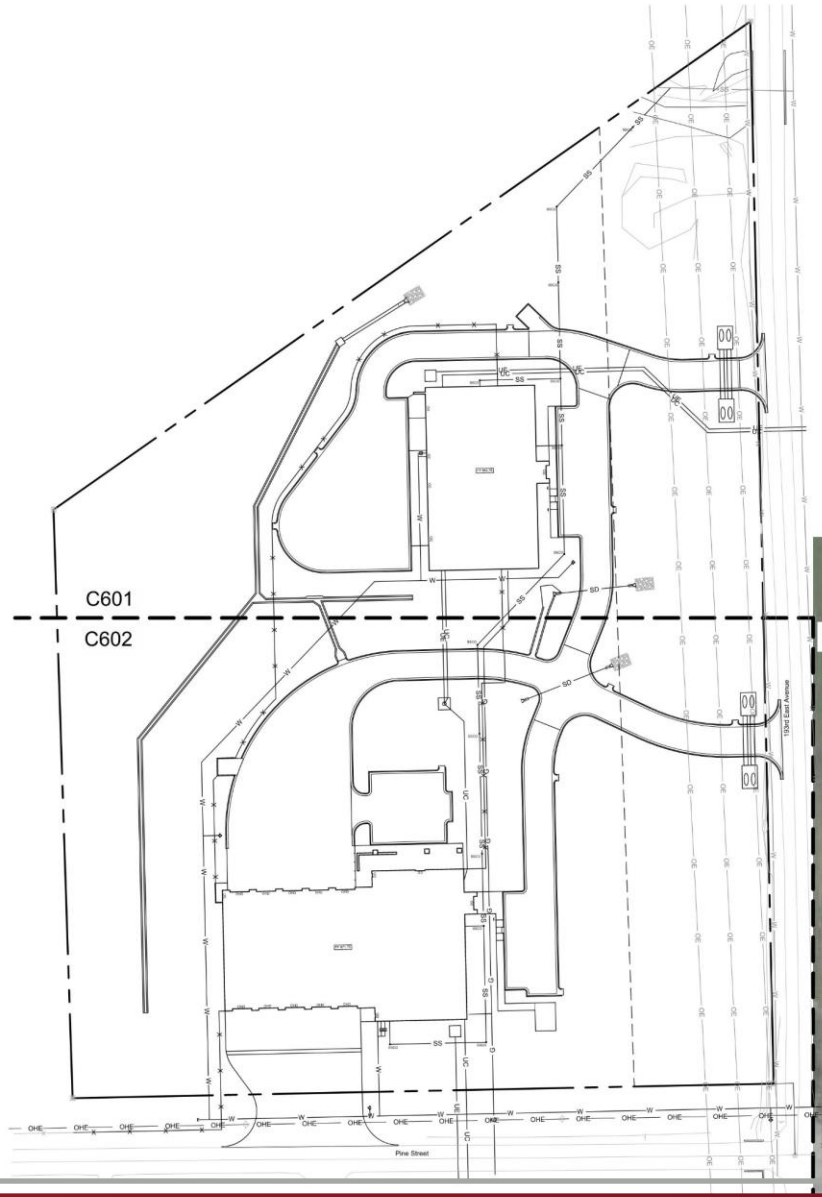



GH2 ARCHITECTS

INTERIM REVIEW ONLY

THESE DOCUMENTS ARE INCOMPLETE. THEY ARE NOT INTENDED TO BE USED FOR PERMITTING, BIDDING, OR CONSTRUCTION.

HAMBY LYNCH PUBLIC SAFETY COMPLEX, VOL I.

N. 193rd E Ave. and E Pine St.
Catoosa, OK 74015

GH2 ARCHITECTS
GH2.COM

GH2 PROJECT NUMBER:
20210238

ISSUE DATE:
09/13/2022

ISSUE:
DESIGN DEVELOPMENT

OTHER ISSUE DATES:

NO.	DESCRIPTION	DATE

UTILITY PLAN

Utility

C600

Call before you dig.

GH2 ARCHITECTS

POLICE STATION

© 2022 GH2 Architects, LLC

GH2 ARCHITECTS

POLICE STATION FLOOR PLAN

GH2 ARCHITECTS

POLICE STATION LOBBY

GH2 ARCHITECTS

POLICE STATION BREAK AREA

GH2 ARCHITECTS

POLICE STATION CONFERENCE

GH2 ARCHITECTS

POLICE STATION LOCKER

GH2 ARCHITECTS

FIRE STATION

© 2022 GH2 Architects, LLC

GH2 ARCHITECTS

FIRE STATION APPARATUS BAY

© 2022 GH2 Architects, LLC

GH2 ARCHITECTS

FIRE STATION BACK OF HOUSE

GH2 ARCHITECTS

FIRE STATION FLOOR PLAN

GH2 ARCHITECTS

FIRE STATION LOBBY

GH2 ARCHITECTS

FIRE STATION CONFERENCE

GH2 ARCHITECTS

FIRE STATION KITCHEN

GH2 ARCHITECTS

FIRE STATION LIVING

GH2 ARCHITECTS

GH2® ARCHITECTS

Design. Service. Solutions.®

www.gh2.com
